### 14,000 m<sup>2</sup>

# Wendy Allison Snr and Jnr Soccer fields







We had been asked by MBRC Moreton Bay Regional Council to engage in the rebuilding of Wendy Allison Soccer field precinct which contains 1 senior full size field and 4 junior fields

#### The process included:

- WHS documentation including Work Method Statement, Site Specific Safety Plan, Construction Schedule
- Service location was required before commencing any works, DIAL BEFORE YOU DIG, plans
- Site establishment and construction fencing to surround site
- Soil tests had been provided by MBRC and soil amendments applied as per the recommendations
- Installation of temporary irrigation system is to be installed prior to turf laying
- Supply and apply soil conditioner, RRA Organics
- Blecavate surfaces
- Laser Level Field including Brush and Final Trim
- Supply and Install Hanceys Turf Premium Wintergreen turf
- Supply and apply Ronstar and starter fertiliser
- Supply and apply pesticide as required
- Supply and apply controlled release fertiliser

#### Maintenance:

- 1st mow and Sweep
- 2nd Mow, Sweep and Topdressing 10mm
- 3rd Mow and Sweep
- 4th Mow, Sweep
- 5th Mow Sweep and Topdressing 10mm
- Maintenance of field for 13 weeks included temporary fence line, mowing and whippering
- Line marking ready for play
- All machinery used during the works was to be of low compaction
- During turf maintenance period the Contractor was to guarantee 100% coverage and establishment of turf through this period
- We had to provide warrantees and certificates for turf and materials used in this project
- "As Constructed Drawings"

# AS THIS SITE WAS SENSITIVE TO ENVIRONMENTAL AND SAFETY REGULATIONS BELOW IS AN OUTLINE WE IMPLEMENT THE FOLLOWING SAFETY PROCESSES AND ACTIONS:

- Site log sheet
- Site induction
- SWMS
- JSA
- PPE
- Safety barrier fencing with dust proof shade cloth
- Site safety signs
- Machinery inspections
- Daily tool box talks
- Mandatory flashing lights and reverse beeper on site equipment
- Mandatory shields and guards fitted to equipment
- Licenced and experienced equipment operators
- Safety policy
- Environmental policy
- Detailed Health and Safety manual with all relevant information easy to refer to and abide by

## ENVIRONMENTAL CONSIDERATIONS SITE SPECIFICS:

- Specified areas for loading and unloading
- Buffer zones
- Coir logs or Silt fencing for silt/erosion control

#### PROGRAM OF WORKS:


Day 1	_Site meeting with stakeholders
Day 2	_Site setup/safety/GPS pick up/service location etc
Day 3	_Herbicide treatments (10 days for die off)
Day 14, 15	_Cultivation and shaping
Day 16-20	_Earthworks- Import material, cultivation, amendments and shape
Day 21	_Final trim and consolidate
Day 22	_Pressure test irrigation system
Day 23, 24	_Supply, install turf and rolling
Day 24	_Fertiliser and pre-emergence
Day 25-90	_Grow in mowing and maintenance program
Day 40	_Rolling
Day 40	_Top dress 1
Day 54	_Top Dress 2
Day 55	_Commission and hand over after maintenance period









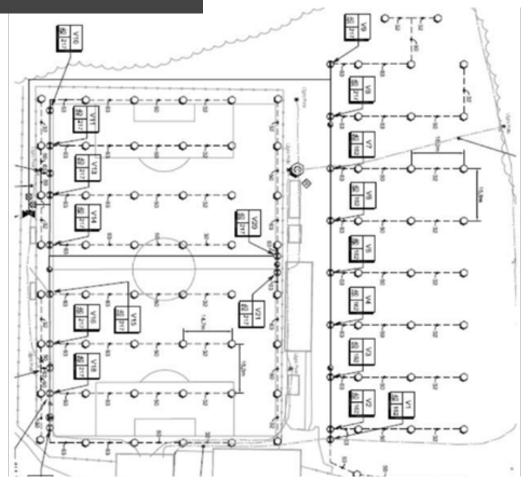

Final shape of the fields taking into consideration of imported soil, existing volumes and run off areas

